BRUHAT BENGALURU MAHANAGARA PALIKE

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to Roads and Drains at Bharathnagara , Sadiq Layout, Anjanadri Layout, Balance Roads and Surrounding Area in Ward No.06 Byatarayanapura Sub Division
	Consultants	:	Civil Pro
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	30-Mar-22
	Project End Date	:	30-Mar-23
	Project Length in Months	:	12 Months

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications and as per the directions of the Engineer-in-charge of the work	Cum	3633.24	3633.24	100	30-03-22	14-04-22	15
2	Providing and laying Plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration	Cum	609.54	609.54	100	14-04-22	24-04-22	10
3	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed, well compacted for wall and Bottom including	Cum	1349.70	1349.70	100	28-04-22	20-05-22	22
4	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks	Tonne	100.91	100.89	100	19-04-22	29-04-22	10
5	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,copmplete. and as per the directions of the	Sqm	3090.71	3090.71	100	20-05-22	31-05-22	11
6	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift, transportation etc ,complete.	Sqm	173.60	173.60	100	20-05-22	31-05-22	11
7	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour	Nos	637.00	637.00	100	25-05-22	04-06-22	10
8	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour Complete as per specifications and directions of the Engineer in charge.	Sqm	114.60	114.60	100	30-05-22	07-06-22	8
9	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications and	Cum	3018.14	3018.14	100	02-06-22	07-06-22	5
10	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications and as per the directions of the Engineer-in-charge of the work	Sqm	6622.05	6622.05	100	02-06-22	07-06-22	5
11	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on	Cum	993.31	993.31	100	04-06-22	11-06-22	7
12	Providing and Constructing dry lean cement concrete mix CC1:5:10 Base with OPC 25mm and down size graded granite metal coarse aggregate at 0.86cum and fine aggregates @ 0.58cum over a prepared sub-base coarse and fine aggregate conforming to IS: 383-2016, aggregate cement ratio not	Cum	1012.42	1012.42	100	09-06-22	19-06-22	10
13	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, using a grade concrete M30 over a prepared base with OPC coarse aggregate @ 0.69cum fine aggregate @ 0.46cum,coarse and fine aggregate confirming to IS:383-2016,with superplastisiser @3lts	Cum	1012.42	1012.42	100	13-06-22	23-06-22	10
E1	Providing Size Stone masonry with hard stone in foundation & plinth with Cement mortar 1:6 and as per the directions of the Engineer-in-charge of the work	Cum	18.82	18.82	100	03-05-22	23-05-22	20

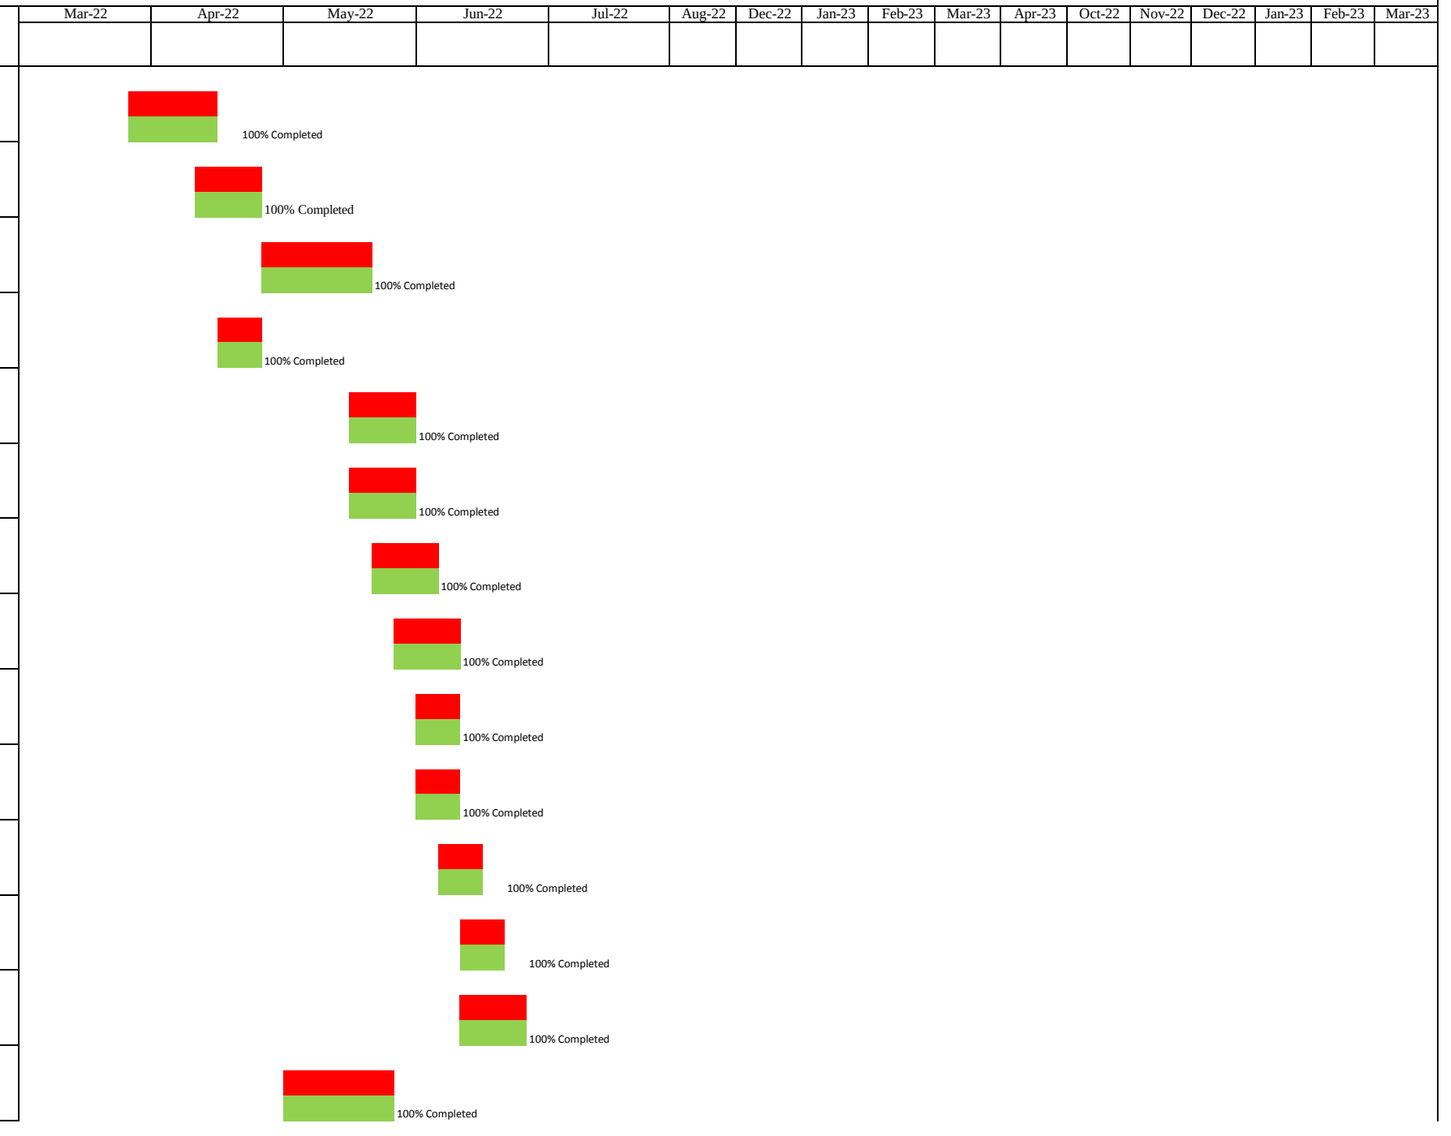

BRUHAT BENGALURU MAHANAGARA PALIKE

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to Roads and Drains at Bharathnagara , Sadiq Layout, Anjanadri Layout, Balance Roads and Surrounding Area in Ward No.06 Byatarayanapura Sub Division
	Consultants	:	Civil Pro
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	30-Mar-22
	Project End Date	:	30-Mar-23
	Project Length in Months	:	12 Months

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Mar-22	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23
E2	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x150x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572:2005 including cost of	Sqm	15.72	15.72	100	03-05-22	13-05-22	10																	

100% Completed

Planned %

Executed %
